



AN ENVIRONMENTAL COMPLIANCE COMPANY

316 W Indiana Ave.
Chesterton, IN 46304

TANK PRESSURE CALCULATION and WATER SENSOR CALIBRATION

EZY CHEK SYSTEMS

FINAL REPORT

PC # and WO #	
NAME and FID #	PHILLIPS 66 #2830
ADDRESS	702 E LINCOLNWAY
CITY/STATE/ZIP	SOUTH BEND, IN 46601
CONTACT	
PHONE	

DATE AND TIME	10-12-22	8:15-14:00
WEATHER	60 CLOUDY	
INVOICE		
TOTAL TANK VOL.	10149	
PRODUCT VOL.	631	
ULLAGE VOL.	9518	
PRODUCT TYPE	REGULAR	
TANK #	1	
Water Level Surrounding Tanks		0.00
BY:	STICK	
WHERE:	MONITORING WELL - TANK BED	

THE ACOUSTIC CHARACTERISTIC OF A LEAK REVEALS:

PASS TIGHT TANK

THIS UNDERGROUND STORAGE TANK PASSES / FAILS THE CRITERIA SET FORTH BY THE U.S. EPA.

PASS ULLAGE (DRY) PORTION OF LEAK

THIS UNDERGROUND STORAGE TANK PASSES / FAILS THE CRITERIA SET FORTH BY THE U.S. EPA.

PASS BELOW PRODUCT LEVEL (WET) PORTION LEAK

THIS UNDERGROUND STORAGE TANK PASSES / FAILS THE CRITERIA SET FORTH BY THE U.S. EPA.

WATER SENSOR INDICATES:

(MARK ONLY ONE)

No Water Intrusion	
Water Intrusion	
Not Applicable	X

OPERATOR INFO

Print Name	Ryan Hartman	Certification #	02-6669
Sign Name	<i>Ryan Hartman</i>	Expiration Date	9/3/23
Testing Company	Midwest Tank Testing	Telephone #	800-975-1436
Address	316 W Indiana Ave.		
City/State/Zip	Chesterton, IN 46304		

	Serial Number
IN-TANK MICROPHONE	M1904009, M1904011, M2003002
ACOUSTIC SIGNAL PROCESSOR	E1638009
PRESSURE SENSOR	41253419, 41121418, 4047126
WATER SENSOR DISPLAY	D2001108, D2001111, D2001112
WATER SENSOR PROBE	P2001299, P1612407, P2102316

Calibration Expiration Date
April-23
April-23
April-23
April-23
April-23

COMMENTS/RECOMMENDATIONS:

TANK PRESSURE CALCULATION and WATER SENSOR CALIBRATION

EZY CHEK SYSTEMS

DATA SHEET

Test Location Information	
PC # and WO #	
NAME and FID #	PHILLIPS 66 #2830
ADDRESS	702 E LINCOLNWAY
CITY/STATE/ZIP	SOUTH BEND, IN 46601
CONTACT	
PHONE	

Certifications
Indiana: UC201511138
Illinois: 002401
Wisconsin: 411637

DATE AND TIME	10-12-22	8:15-14:00
WEATHER	60 CLOUDY	
INVOICE		
TOTAL TANK VOL.	10149	
PRODUCT VOL.	631	
ULLAGE VOL.	9518	
PRODUCT TYPE	REGULAR	
TANK #	1	
Water Level Surrounding Tanks		0.00
BY:	MEASURING STICK	
WHERE:	MONITORING WELL - TANK BED	

TANK TIGHTNESS TEST - (TTT) PRESSURE SENSOR CALCULATION

10.50	x	0.026	=	0.273	PSI (1)
INCHES OF PRODUCT		WEIGHT OF PRODUCT			
0.00	x	.036	=	0.000	PSI (2)
INCHES OF WATER IN TANK					
Line 1 + Line 2 = Total Positive Head Pressure In Tank			=	0.273	PSI (3)
0.00	x	.036	=	0.000	PSI (4)
INCHES OF WATER OUTSIDE TANK					
Total Head Pressure Minus Outside Water Pressure			=	0.273	+/- PSI (5)
Always add .5 PSI			+	0.500	PSI (6)
NOTE: If Line 6 is Less Than .5 PSI Line 7 Shall be .5 PSI					
TEST PRESSURE			=	0.773	+/- PSI (7)

ACOUSTIC TEST TIME


	Time	Pressure
Baseline Background:	10:12 AM	0.0
Blower Started:	10:15 AM	0.0
Test Pressure Reached:	10:44 AM	0.832
Blower Turned Off:	10:44 AM	0.832
Test Began:	10:45 AM	0.831
Test Ended:	10:47 AM	0.829

EQUIPMENT CALIBRATION DUE DATE AND SERIAL NUMBERS

	Serial Number	Calibration Due Date
In-Tank Microphone	M1904009, M1904011, M2003002	April-23
Acoustic Signal Processor	E1638009	April-23
Pressure Sensor	41253419, 41121418, 4047126	April-23
Water Sensor Display	D2001108, D2001111, D2001112	April-23
Water Sensor Probe	P2001299, P1612407, P2102316	April-23

WATER SENSOR CALIBRATION

Added:	N/A	N/A	N/A
Average:	0		
Calculation for Test Period:			
0 ÷ 3780 = 0.000 ÷ .05	0.000	x 60	0 minutes
Avg. Cal.	"A" Factor	Min.	Time of Test
Water Intrusion Test Period:			
Began:	N/A		
Ended:	N/A		

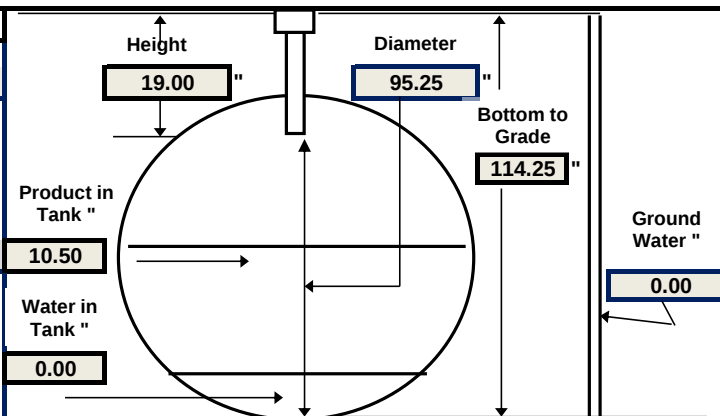



AN ENVIRONMENTAL COMPLIANCE COMPANY

316 W Indiana Ave.
Chesterton, IN 46304

TANK PRESSURE CALCULATION and WATER SENSOR CALIBRATION

EZY CHEK SYSTEMS

FINAL REPORT

PC # and WO #	
NAME and FID #	PHILLIPS 66 #2830
ADDRESS	702 E LINCOLNWAY
CITY/STATE/ZIP	SOUTH BEND, IN 46601
CONTACT	
PHONE	

DATE AND TIME	10-12-22	8:15-14:00
WEATHER	60 CLOUDY	
INVOICE		
TOTAL TANK VOL.	7896	
PRODUCT VOL.	113	
ULLAGE VOL.	7783	
PRODUCT TYPE	MID	
TANK #	2	
Water Level Surrounding Tanks		0.00
BY:	STICK	
WHERE:	MONITORING WELL - TANK BED	

THE ACOUSTIC CHARACTERISTIC OF A LEAK REVEALS:

PASS TIGHT TANK

THIS UNDERGROUND STORAGE TANK PASSES / FAILS THE CRITERIA SET FORTH BY THE U.S. EPA.

PASS ULLAGE (DRY) PORTION OF LEAK

THIS UNDERGROUND STORAGE TANK PASSES / FAILS THE CRITERIA SET FORTH BY THE U.S. EPA.

PASS BELOW PRODUCT LEVEL (WET) PORTION LEAK

THIS UNDERGROUND STORAGE TANK PASSES / FAILS THE CRITERIA SET FORTH BY THE U.S. EPA.

WATER SENSOR INDICATES:

(MARK ONLY ONE)

No Water Intrusion

Water Intrusion

Not Applicable

X

OPERATOR INFO

Print Name	Ryan Hartman	Certification #	02-6669
Sign Name	<i>Ryan Hartman</i>	Expiration Date	9/3/23
Testing Company	Midwest Tank Testing	Telephone #	800-975-1436
Address	316 W Indiana Ave.		
City/State/Zip	Chesterton, IN 46304		

IN-TANK MICROPHONE	Serial Number
	M1904009, M1904011, M2003002
ACOUSTIC SIGNAL PROCESSOR	E1638009
PRESSURE SENSOR	41253419, 41121418, 4047126
WATER SENSOR DISPLAY	D2001108, D2001111, D2001112
WATER SENSOR PROBE	P2001299, P1612407, P2102316

Calibration Expiration Date
April-23
April-23
April-23
April-23
April-23

COMMENTS/RECOMMENDATIONS:

TANK PRESSURE CALCULATION and WATER SENSOR CALIBRATION

EZY CHEK SYSTEMS

DATA SHEET

Test Location Information		Certifications
PC # and WO #		Indiana: UC201511138
NAME and FID #	PHILLIPS 66 #2830	Illinois: 002401
ADDRESS	702 E LINCOLNWAY	Wisconsin: 411637
CITY/STATE/ZIP	SOUTH BEND, IN 46601	
CONTACT		
PHONE		

DATE AND TIME	10-12-22	8:15-14:00
WEATHER	60 CLOUDY	
INVOICE		
TOTAL TANK VOL.	7896	
PRODUCT VOL.	113	
ULLAGE VOL.	7783	
PRODUCT TYPE	MID	
TANK #	2	
Water Level Surrounding Tanks		0.00
BY:	MEASURING STICK	
WHERE:	MONITORING WELL - TANK BED	

TANK TIGHTNESS TEST - (TTT) PRESSURE SENSOR CALCULATION

4.00	x	0.026	=	0.104	PSI (1)
INCHES OF PRODUCT		WEIGHT OF PRODUCT			
0.00	x	.036	=	0.000	PSI (2)
INCHES OF WATER IN TANK					
Line 1 + Line 2 = Total Positive Head Pressure In Tank			=	0.104	PSI (3)
0.00	x	.036	=	0.000	PSI (4)
INCHES OF WATER OUTSIDE TANK					
Total Head Pressure Minus Outside Water Pressure			=	0.104	+/- PSI (5)
Always add .5 PSI			+	0.500	PSI (6)
NOTE: If Line 6 is Less Than .5 PSI Line 7 Shall be .5 PSI					
TEST PRESSURE			=	0.604	+/- PSI (7)

ACOUSTIC TEST TIME


	Time	Pressure
Baseline Background:	10:14 AM	0.0
Blower Started:	10:15 AM	0.0
Test Pressure Reached:	10:44 AM	0.856
Blower Turned Off:	10:44 AM	0.856
Test Began:	10:49 AM	0.846
Test Ended:	10:51 AM	0.842

EQUIPMENT CALIBRATION DUE DATE AND SERIAL NUMBERS

	Serial Number	Calibration Due Date
In-Tank Microphone	M1904009, M1904011, M2003002	April-23
Acoustic Signal Processor	E1638009	April-23
Pressure Sensor	41253419, 41121418, 4047126	April-23
Water Sensor Display	D2001108, D2001111, D2001112	April-23
Water Sensor Probe	P2001299, P1612407, P2102316	April-23

WATER SENSOR CALIBRATION

Added:	N/A	N/A	N/A
Average:	0		
Calculation for Test Period:			
0 ÷ 3780 = 0.000 ÷ .05	0.000	x 60	0 minutes
Avg. Cal.	"A" Factor	Min.	Time of Test
Water Intrusion Test Period:			
Began:	N/A		
Ended:	N/A		

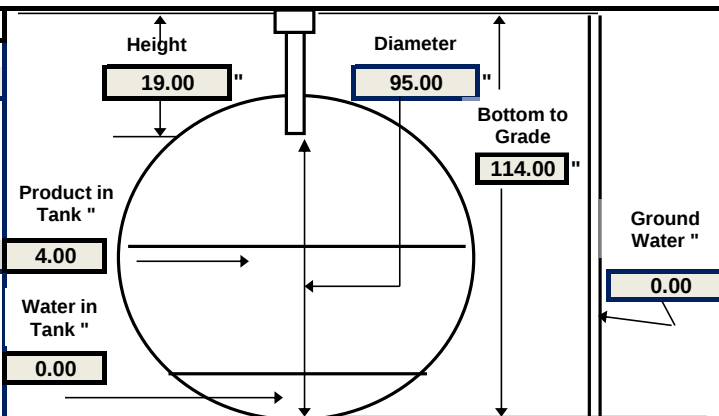



AN ENVIRONMENTAL COMPLIANCE COMPANY

316 W Indiana Ave.
Chesterton, IN 46304

TANK PRESSURE CALCULATION and WATER SENSOR CALIBRATION

EZY CHEK SYSTEMS

FINAL REPORT

PC # and WO #	
NAME and FID #	PHILLIPS 66 #2830
ADDRESS	702 E LINCOLNWAY
CITY/STATE/ZIP	SOUTH BEND, IN 46601
CONTACT	
PHONE	

DATE AND TIME	10-12-22	8:15-14:00
WEATHER	60 CLOUDY	
INVOICE		
TOTAL TANK VOL.	1998	
PRODUCT VOL.	623	
ULLAGE VOL.	1375	
PRODUCT TYPE	PREMIUM	
TANK #	3	
Water Level Surrounding Tanks		0.00
BY:	STICK	
WHERE:	MONITORING WELL - TANK BED	

THE ACOUSTIC CHARACTERISTIC OF A LEAK REVEALS:

PASS TIGHT TANK

THIS UNDERGROUND STORAGE TANK PASSES / FAILS THE CRITERIA SET FORTH BY THE U.S. EPA.

PASS ULLAGE (DRY) PORTION OF LEAK

THIS UNDERGROUND STORAGE TANK PASSES / FAILS THE CRITERIA SET FORTH BY THE U.S. EPA.

PASS BELOW PRODUCT LEVEL (WET) PORTION LEAK

THIS UNDERGROUND STORAGE TANK PASSES / FAILS THE CRITERIA SET FORTH BY THE U.S. EPA.

WATER SENSOR INDICATES:

(MARK ONLY ONE)

No Water Intrusion	
Water Intrusion	
Not Applicable	X

OPERATOR INFO

Print Name	Ryan Hartman	Certification #	02-6669
Sign Name	<i>Ryan Hartman</i>	Expiration Date	9/3/23
Testing Company	Midwest Tank Testing	Telephone #	800-975-1436
Address	316 W Indiana Ave.		
City/State/Zip	Chesterton, IN 46304		

IN-TANK MICROPHONE	Serial Number M1904009, M1904011, M2003002
ACOUSTIC SIGNAL PROCESSOR	E1638009
PRESSURE SENSOR	41253419, 41121418, 4047126
WATER SENSOR DISPLAY	D2001108, D2001111, D2001112
WATER SENSOR PROBE	P2001299, P1612407, P2102316

Calibration Expiration Date
April-23
April-23
April-23
April-23
April-23

COMMENTS/RECOMMENDATIONS:

TANK PRESSURE CALCULATION and WATER SENSOR CALIBRATION

EZY CHEK SYSTEMS

DATA SHEET

Test Location Information		Certifications
PC # and WO #		Indiana: UC201511138
NAME and FID #	PHILLIPS 66 #2830	Illinois: 002401
ADDRESS	702 E LINCOLNWAY	Wisconsin: 411637
CITY/STATE/ZIP	SOUTH BEND, IN 46601	
CONTACT		
PHONE		

DATE AND TIME	10-12-22	8:15-14:00
WEATHER	60 CLOUDY	
INVOICE		
TOTAL TANK VOL.	1998	
PRODUCT VOL.	623	
ULLAGE VOL.	1375	
PRODUCT TYPE	PREMIUM	
TANK #	3	
Water Level Surrounding Tanks		0.00
BY:	MEASURING STICK	
WHERE:	MONITORING WELL - TANK BED	

TANK TIGHTNESS TEST - (TTT) PRESSURE SENSOR CALCULATION

22.00	x	0.026	=	0.572	PSI (1)
INCHES OF PRODUCT		WEIGHT OF PRODUCT			
0.00	x	.036	=	0.000	PSI (2)
INCHES OF WATER IN TANK					
Line 1 + Line 2 = Total Positive Head Pressure In Tank			=	0.572	PSI (3)
0.00	x	.036	=	0.000	PSI (4)
INCHES OF WATER OUTSIDE TANK					
Total Head Pressure Minus Outside Water Pressure			=	0.572	+/- PSI (5)
Always add .5 PSI			+	0.500	PSI (6)
NOTE: If Line 6 is Less Than .5 PSI Line 7 Shall be .5 PSI					
TEST PRESSURE			=	1.072	+/- PSI (7)

ACOUSTIC TEST TIME


	Time	Pressure
Baseline Background:	10:13 AM	0.0
Blower Started:	10:15 AM	0.0
Test Pressure Reached:	10:44 AM	1.148
Blower Turned Off:	10:44 AM	1.148
Test Began:	10:47 AM	1.140
Test Ended:	10:49 AM	1.136

EQUIPMENT CALIBRATION DUE DATE AND SERIAL NUMBERS

	Serial Number	Calibration Due Date
In-Tank Microphone	M1904009, M1904011, M2003002	April-23
Acoustic Signal Processor	E1638009	April-23
Pressure Sensor	41253419, 41121418, 4047126	April-23
Water Sensor Display	D2001108, D2001111, D2001112	April-23
Water Sensor Probe	P2001299, P1612407, P2102316	April-23

WATER SENSOR CALIBRATION

Added:	N/A	N/A	N/A
Average:	0		
Calculation for Test Period:			
0 ÷ 3780 = 0.000 ÷ .05	0.000	x 60	0 minutes
Avg. Cal.	"A" Factor	Min.	Time of Test
Water Intrusion Test Period:			
Began:	N/A		
Ended:	N/A		

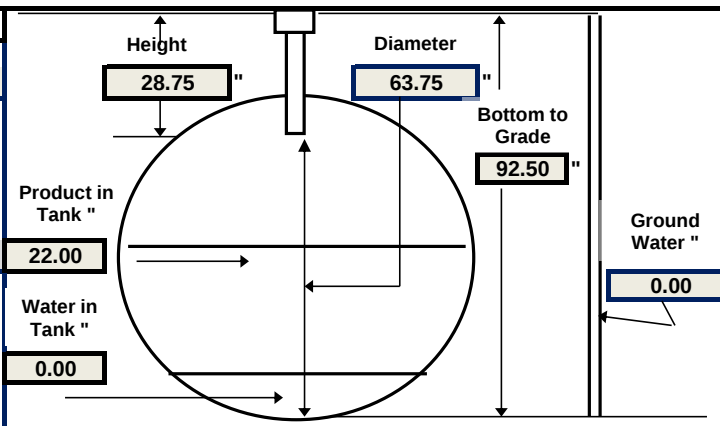



AN ENVIRONMENTAL COMPLIANCE COMPANY

316 W Indiana Ave.
Chesterton, IN 46304

TANK PRESSURE CALCULATION and WATER SENSOR CALIBRATION

EZY CHEK SYSTEMS

FINAL REPORT

PC # and WO #	
NAME and FID #	PHILLIPS 66 #2830
ADDRESS	702 E LINCOLNWAY
CITY/STATE/ZIP	SOUTH BEND, IN 46601
CONTACT	
PHONE	

DATE AND TIME	10-12-22	8:15-14:00
WEATHER	60 CLOUDY	
INVOICE		
TOTAL TANK VOL.	3000	
PRODUCT VOL.	128	
ULLAGE VOL.	2872	
PRODUCT TYPE	DIESEL	
TANK #	4	
Water Level Surrounding Tanks		0.00
BY:	STICK	
WHERE:	MONITORING WELL - TANK BED	

THE ACOUSTIC CHARACTERISTIC OF A LEAK REVEALS:

PASS TIGHT TANK

THIS UNDERGROUND STORAGE TANK PASSES / FAILS THE CRITERIA SET FORTH BY THE U.S. EPA.

PASS ULLAGE (DRY) PORTION OF LEAK

THIS UNDERGROUND STORAGE TANK PASSES / FAILS THE CRITERIA SET FORTH BY THE U.S. EPA.

PASS BELOW PRODUCT LEVEL (WET) PORTION LEAK

THIS UNDERGROUND STORAGE TANK PASSES / FAILS THE CRITERIA SET FORTH BY THE U.S. EPA.

WATER SENSOR INDICATES:

(MARK ONLY ONE)

No Water Intrusion

Water Intrusion

Not Applicable

X

OPERATOR INFO

Print Name	Ryan Hartman	Certification #	02-6669
Sign Name	<i>Ryan Hartman</i>	Expiration Date	9/3/23
Testing Company	Midwest Tank Testing	Telephone #	800-975-1436
Address	316 W Indiana Ave.		
City/State/Zip	Chesterton, IN 46304		

	Serial Number
IN-TANK MICROPHONE	M1904009, M1904011, M2003002
ACOUSTIC SIGNAL PROCESSOR	E1638009
PRESSURE SENSOR	41253419, 41121418, 4047126
WATER SENSOR DISPLAY	D2001108, D2001111, D2001112
WATER SENSOR PROBE	P2001299, P1612407, P2102316

Calibration Expiration Date
April-23
April-23
April-23
April-23
April-23

COMMENTS/RECOMMENDATIONS:

TANK PRESSURE CALCULATION and WATER SENSOR CALIBRATION

EZY CHEK SYSTEMS

DATA SHEET

Test Location Information		Certifications
PC # and WO #		Indiana: UC201511138
NAME and FID #	PHILLIPS 66 #2830	Illinois: 002401
ADDRESS	702 E LINCOLNWAY	Wisconsin: 411637
CITY/STATE/ZIP	SOUTH BEND, IN 46601	
CONTACT		
PHONE		

DATE AND TIME	10-12-22	8:15-14:00
WEATHER	60 CLOUDY	
INVOICE		
TOTAL TANK VOL.	3000	
PRODUCT VOL.	128	
ULLAGE VOL.	2872	
PRODUCT TYPE	DIESEL	
TANK #	4	
Water Level Surrounding Tanks		0.00
BY:	MEASURING STICK	
WHERE:	MONITORING WELL - TANK BED	

TANK TIGHTNESS TEST - (TTT) PRESSURE SENSOR CALCULATION

8.00	x	0.031	=	0.248	PSI (1)
INCHES OF PRODUCT		WEIGHT OF PRODUCT			
0.00	x	.036	=	0.000	PSI (2)
INCHES OF WATER IN TANK					
Line 1 + Line 2 = Total Positive Head Pressure In Tank			=	0.248	PSI (3)
0.00	x	.036	=	0.000	PSI (4)
INCHES OF WATER OUTSIDE TANK					
Total Head Pressure Minus Outside Water Pressure			=	0.248	+/- PSI (5)
Always add .5 PSI			+	0.500	PSI (6)
NOTE: If Line 6 is Less Than .5 PSI Line 7 Shall be .5 PSI					
TEST PRESSURE			=	0.748	+/- PSI (7)

ACOUSTIC TEST TIME


	Time	Pressure
Baseline Background:	11:42 AM	0.0
Blower Started:	11:44 AM	0.0
Test Pressure Reached:	11:48 AM	0.791
Blower Turned Off:	11:48 AM	0.791
Test Began:	11:49 AM	0.790
Test Ended:	11:51 AM	0.788

EQUIPMENT CALIBRATION DUE DATE AND SERIAL NUMBERS

	Serial Number	Calibration Due Date
In-Tank Microphone	M1904009, M1904011, M2003002	April-23
Acoustic Signal Processor	E1638009	April-23
Pressure Sensor	41253419, 41121418, 4047126	April-23
Water Sensor Display	D2001108, D2001111, D2001112	April-23
Water Sensor Probe	P2001299, P1612407, P2102316	April-23

WATER SENSOR CALIBRATION

Added:	N/A	N/A	N/A
Average:	0		
Calculation for Test Period:			
0 ÷ 3780 = 0.000 ÷ .05	0.000	x 60	0 minutes
Avg. Cal.	"A" Factor	Min.	Time of Test
Water Intrusion Test Period:			
Began:	N/A		
Ended:	N/A		

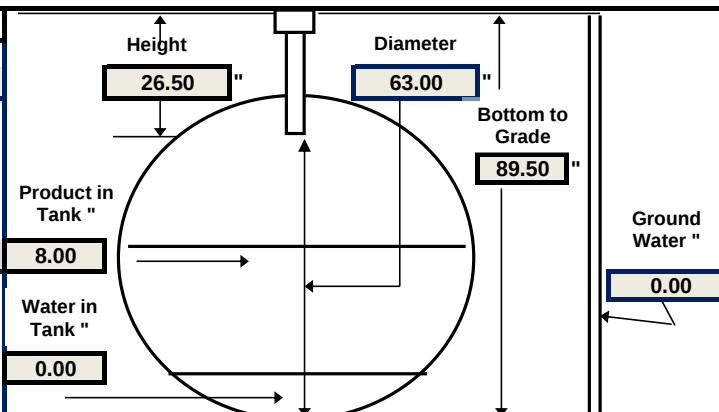



AN ENVIRONMENTAL COMPLIANCE COMPANY

316 W Indiana Ave.
Chesterton, IN 46304

TANK PRESSURE CALCULATION and WATER SENSOR CALIBRATION

EZY CHEK SYSTEMS

FINAL REPORT

PC # and WO #	
NAME and FID #	PHILLIPS 66 #2830
ADDRESS	702 E LINCOLNWAY
CITY/STATE/ZIP	SOUTH BEND, IN 46601
CONTACT	
PHONE	

DATE AND TIME	10-12-22	8:15-14:00
WEATHER	60 CLOUDY	
INVOICE		
TOTAL TANK VOL.		
PRODUCT VOL.		
ULLAGE VOL.		
PRODUCT TYPE	KERO	
TANK #	5	
Water Level Surrounding Tanks		0.00
BY:	STICK	
WHERE:	MONITORING WELL - TANK BED	

THE ACOUSTIC CHARACTERISTIC OF A LEAK REVEALS:

PASS TIGHT TANK

THIS UNDERGROUND STORAGE TANK PASSES / FAILS THE CRITERIA SET FORTH BY THE U.S. EPA.

PASS ULLAGE (DRY) PORTION OF LEAK

THIS UNDERGROUND STORAGE TANK PASSES / FAILS THE CRITERIA SET FORTH BY THE U.S. EPA.

PASS BELOW PRODUCT LEVEL (WET) PORTION LEAK

THIS UNDERGROUND STORAGE TANK PASSES / FAILS THE CRITERIA SET FORTH BY THE U.S. EPA.

WATER SENSOR INDICATES:

(MARK ONLY ONE)

No Water Intrusion

Water Intrusion

Not Applicable

X

OPERATOR INFO

Print Name	Ryan Hartman	Certification #	02-6669
Sign Name	<i>Ryan Hartman</i>	Expiration Date	9/3/23
Testing Company	Midwest Tank Testing	Telephone #	800-975-1436
Address	316 W Indiana Ave.		
City/State/Zip	Chesterton, IN 46304		

IN-TANK MICROPHONE	Serial Number
	M1904009, M1904011, M2003002
ACOUSTIC SIGNAL PROCESSOR	E1638009
PRESSURE SENSOR	41253419, 41121418, 4047126
WATER SENSOR DISPLAY	D2001108, D2001111, D2001112
WATER SENSOR PROBE	P2001299, P1612407, P2102316

Calibration Expiration Date
April-23
April-23
April-23
April-23
April-23

COMMENTS/RECOMMENDATIONS:

TANK PRESSURE CALCULATION and WATER SENSOR CALIBRATION

EZY CHEK SYSTEMS

DATA SHEET

DATE AND TIME	10-12-22	8:15-14:00
WEATHER	60 CLOUDY	
INVOICE		
TOTAL TANK VOL.		
PRODUCT VOL.		
ULLAGE VOL.		
PRODUCT TYPE	KERO	
TANK #	5	
Water Level Surrounding Tanks		0.00
BY:	MEASURING STICK	
WHERE:	MONITORING WELL - TANK BED	

Test Location Information		Certifications
PC # and WO #		Indiana: UC201511138
NAME and FID #	PHILLIPS 66 #2830	Illinois: 002401
ADDRESS	702 E LINCOLNWAY	Wisconsin: 411637
CITY/STATE/ZIP	SOUTH BEND, IN 46601	
CONTACT		
PHONE		

TANK TIGHTNESS TEST - (TTT) PRESSURE SENSOR CALCULATION

3.00	x	0.029	=	0.087	PSI (1)
INCHES OF PRODUCT		WEIGHT OF PRODUCT			
0.00	x	.036	=	0.000	PSI (2)
INCHES OF WATER IN TANK					
Line 1 + Line 2 = Total Positive Head Pressure In Tank			=	0.087	PSI (3)
0.00	x	.036	=	0.000	PSI (4)
INCHES OF WATER OUTSIDE TANK					
Total Head Pressure Minus Outside Water Pressure			=	0.087	+/- PSI (5)
Always add .5 PSI			+	0.500	PSI (6)
NOTE: If Line 6 is Less Than .5 PSI Line 7 Shall be .5 PSI					
TEST PRESSURE			=	0.587	+/- PSI (7)

ACOUSTIC TEST TIME

	Time	Pressure
Baseline Background:	11:43 AM	0.0
Blower Started:	11:44 AM	0.0
Test Pressure Reached:	11:48 AM	0.754
Blower Turned Off:	11:48 AM	0.754
Test Began:	11:51 AM	0.750
Test Ended:	11:53 AM	0.747

EQUIPMENT CALIBRATION DUE DATE AND SERIAL NUMBERS

	Serial Number	Calibration Due Date
In-Tank Microphone	M1904009, M1904011, M2003002	April-23
Acoustic Signal Processor	E1638009	April-23
Pressure Sensor	41253419, 41121418, 4047126	April-23
Water Sensor Display	D2001108, D2001111, D2001112	April-23
Water Sensor Probe	P2001299, P1612407, P2102316	April-23

WATER SENSOR CALIBRATION

Added:	N/A	N/A	N/A
Average:	0		
Calculation for Test Period:			
0 ÷ 3780 = 0.000 ÷ .05	0.000	x 60	0 minutes
Avg. Cal.	"A" Factor	Min.	Time of Test
Water Intrusion Test Period:			
Began:	N/A		
Ended:	N/A		

