



## UST TESTING/INSPECTION RESULTS SUMMARY

OWNER NAME: Tanks Data  
OWNER ADDRESS: 1245 South Main Street  
OWNER CITY/STATE/ZIP: Elkhart, IN 46516  
  
TESTING DATE: 8/29/2023

LOCATION NAME: Citgo Elkhart  
LOCATION ADDRESS: 1245 South Main Street  
LOCATION CITY/STATE: Elkhart, IN 46516  
LOCATION FID#: 01633

METHOD OF TANK LEAK DETECTION: NA  
METHOD OF PIPING LEAK DETECTION: PRESSURE  
TYPE OF UNDERGROUND PIPING: STEEL

### ANNUAL TESTING/INSPECTIONS

#### AUTOMATIC TANK GAUGE TEST

COMPLETED

| TANK NO | PRODUCT | BRAND/MODEL | RESULT |
|---------|---------|-------------|--------|
| 1       | RUL     | INCON       | PASS   |
| 2       | DSL     | INCON       | PASS   |
| 3       | PUL     | INCON       | FAIL   |
|         |         |             |        |
|         |         |             |        |
|         |         |             |        |

#### PRODUCT LINE TEST

COMPLETED

Product line must be within manufacturer's criteria of +/- .050 GPH.

| LINE NO | PRODUCT | RESULT | AMT OF CHG/GPH |
|---------|---------|--------|----------------|
| 1       | RUL     | PASS   | 0              |
| 2       | DSL     | PASS   | 0              |
| 3       | PUL     | PASS   | 0              |
|         |         |        |                |
|         |         |        |                |
|         |         |        |                |

#### LEAK DETECTOR TEST

COMPLETED

| LINE NO | PRODUCT | TYPE | RESULT |
|---------|---------|------|--------|
| 1       | RUL     | MLLD | PASS   |
| 2       | DSL     | MLLD | PASS   |
| 3       | PUL     | MLLD | PASS   |
|         |         |      |        |
|         |         |      |        |
|         |         |      |        |

#### LIQUID SENSOR FUNCTIONALITY TEST

NOT PERFORMED

| LOCATION | PRODUCT | TYPE | RESULT |
|----------|---------|------|--------|
|          |         |      |        |
|          |         |      |        |
|          |         |      |        |
|          |         |      |        |
|          |         |      |        |
|          |         |      |        |
|          |         |      |        |
|          |         |      |        |
|          |         |      |        |
|          |         |      |        |
|          |         |      |        |

#### LEGEND:

|      |                  |
|------|------------------|
| RUL  | Regular Unleaded |
| DSL  | Diesel           |
| PUL  | Premium Unleaded |
| KER  | Kerosene         |
| ODSL | Off Road Diesel  |
| REC  | Recreational     |

Thank you for the opportunity to partner with you in your UST Compliance needs!




## SITE PHOTOS


TEST DATE: 8/29/2023  
LOCATION NAME: Citgo Elkhart  
LOCATION ADDRESS: 1245 South Main Street  
LOCATION CITY/STATE: Elkhart, IN 46516  
LOCATION PHONE: 0  
LOCATION CONTACT: Virendar Kumar

OWNER NAME: Tanks Data  
OWNER ADDRESS: 1245 South Main Street  
OWNER CITY/STATE/ZIP: Elkhart, IN 46516  
LOCATION FID#: 01633  
WORK ORDER NO: NE-0543

DSL ATG PROBE TEST

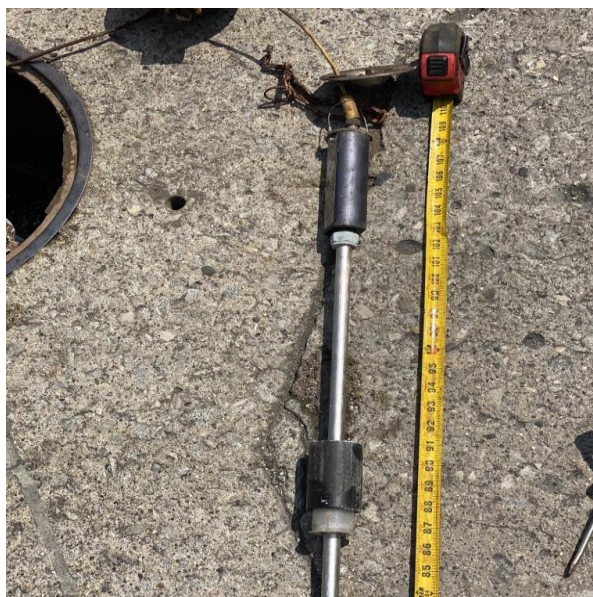

RUL ATG PROBE TEST

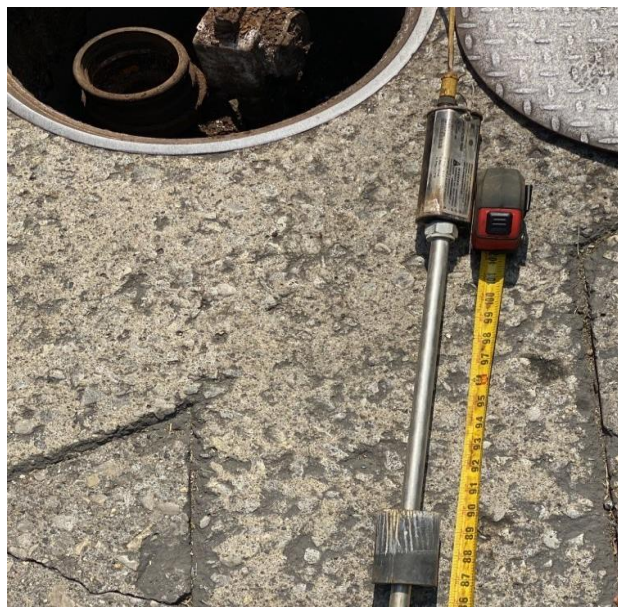



## CERTIFICATION VERIFICATION

Tanks Data  
1245 South Main Street  
Elkhart, IN 46516

Testing Date: 8/29/2023  
Citgo Elkhart  
Location of Test: 1245 South Main Street  
Elkhart, IN 46516  
Site FID#: 01633  
Service Technician: 0  
Certified Technician: RONNIE BROWN

Midwest ECS has completed the following tests/inspections at the above noted location:

|                               |   |
|-------------------------------|---|
| ATG Functionality             | X |
| Leak Detector                 | X |
| Elec Line Leak Detector       |   |
| Product Line Testing          | X |
| Liquid Sensor Functionality   |   |
| Spill Bucket                  |   |
| Containment Hydrostatic Sump  |   |
| Overfill Equipment Inspection |   |
| Overfill Alarm                |   |
| Vent Valve                    |   |
| Interstitial                  |   |
| Non-Volumetric Tank Tightness |   |
| Shear Valve Inspection        |   |

I, RONNIE BROWN, the certified technician, was present throughout the duration of the testing and/or inspection performed by Midwest ECS at the above address on the above date. I affirm that the testing was done in accordance with Rule 329 IAC 9 and 40CFR Part 80, is accurate based upon the results received and that these forms accurately reflects the results of the testing and/or inspection.

Technician Signature:

*Ronnie Brown*

Technician Printed Name:

RONNIE BROWN

Date & Time:

8/29/2023 12:00

|                                                                                     |                                                                                     |
|-------------------------------------------------------------------------------------|-------------------------------------------------------------------------------------|
|  |  |
| <b>Underground Storage Tank</b>                                                     |                                                                                     |
| RONNIE F BROWN<br>4400 W CR 350 S<br>MUNCIE, INDIANA                                |                                                                                     |
| STATE/PERMIT #<br>UC112255                                                          | ISSUE<br>01/24/2023                                                                 |
| EFFECTIVE<br>01/24/2023                                                             | EXPIRATION<br>01/23/2025                                                            |
| <b>DISCIPLINES</b>                                                                  |                                                                                     |
| <input checked="" type="checkbox"/> Installation or Retrofitting                    | <input type="checkbox"/> Decommissioning Closure                                    |
| <input type="checkbox"/> Cathodic Protection                                        | <input type="checkbox"/> Decommissioning Removal                                    |

I attest with my signature below, that this technician was present onsite for testing as described above.
